


Analysis of Dependencies:

Task	Description	Dependencies	Duration(days)
A	Requirement Analysis	-	1
B	UI Design(Front End Development)	A	3
C	Backend Development	A	4
D	Database Setup(Connection to MongoDB)	C	2
E	API Integration	B,C	1
F	Testing	D,E	6
G	Deployment	F	2


Network Diagram

Note: Used Circular nodes and not square grids because app used to draw did not have square grid available.

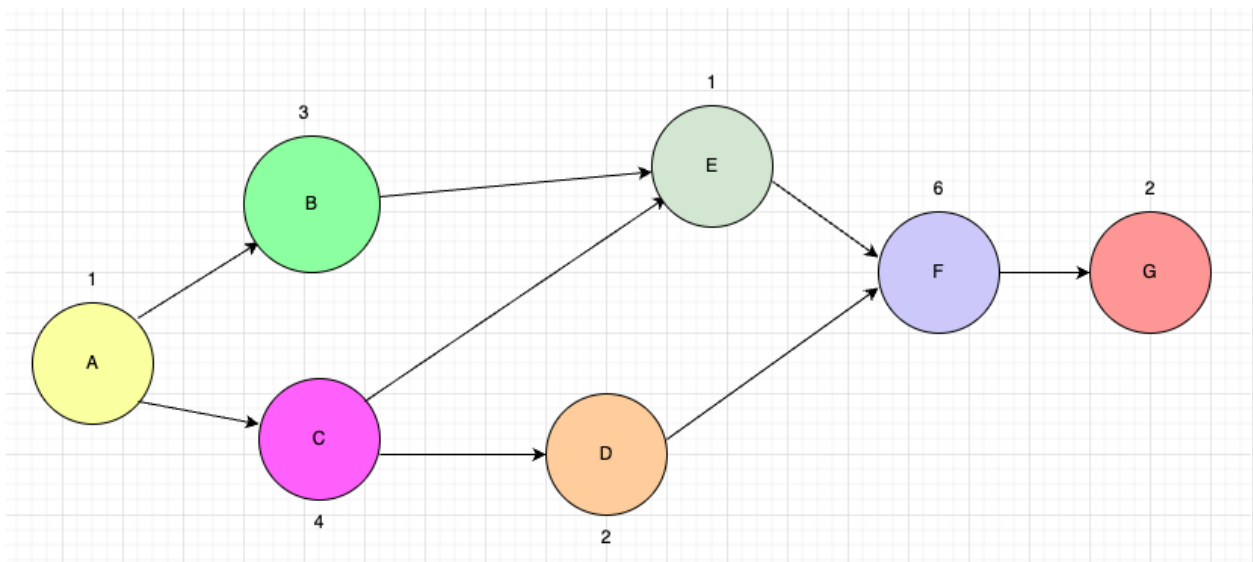

Determining the Critical Path:

There are 2 paths to the end node:

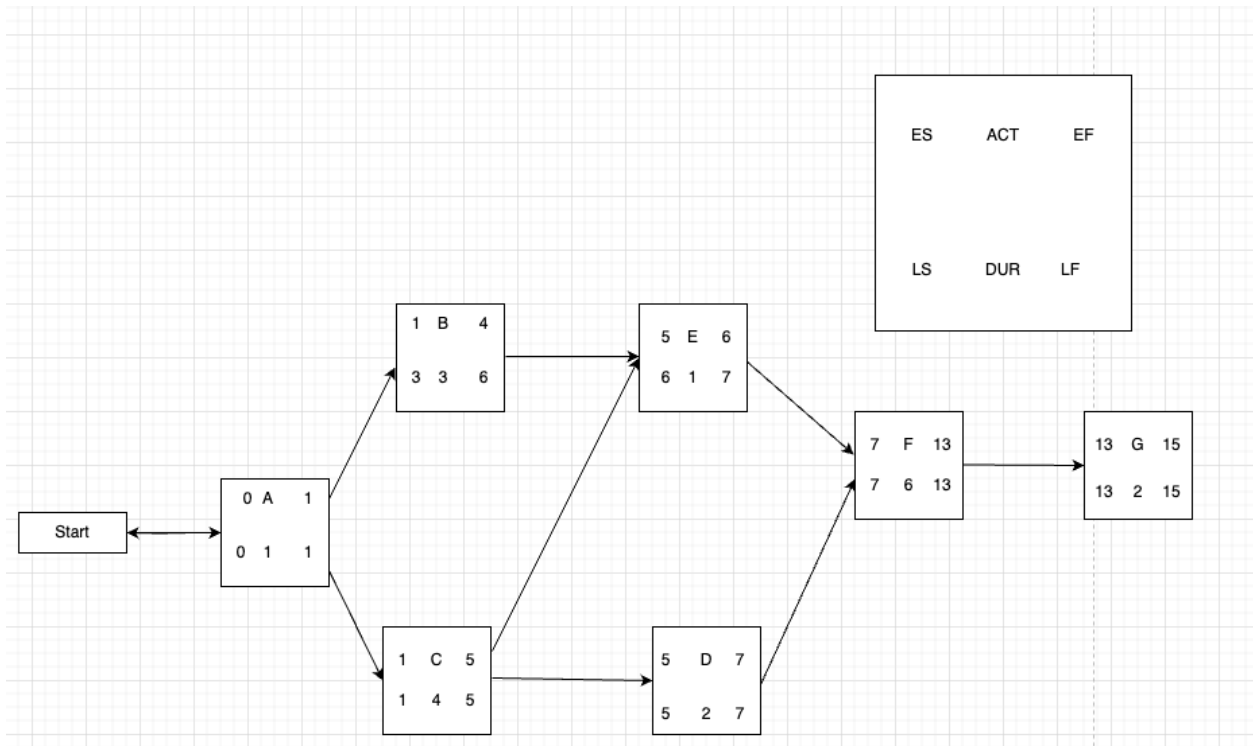

Findings

Our critical path is A-C-D-F-G. These are the activities with 0 slack.

If we delayed any of these projects in the critical part, it will extend our total project duration.

B and E duration can be extended without affecting the total duration.

In order to keep the print in schedule, the following was done:

- The team coordinated regular meetings to ensure that each individual was up to task.
- Incorporated regular check-ins via Discord to ensure that each member of the team was performing tasks that they had been assigned to.
- Ensuring that each individual within the team is responsible for work that they could likely complete within the required timeframe.
